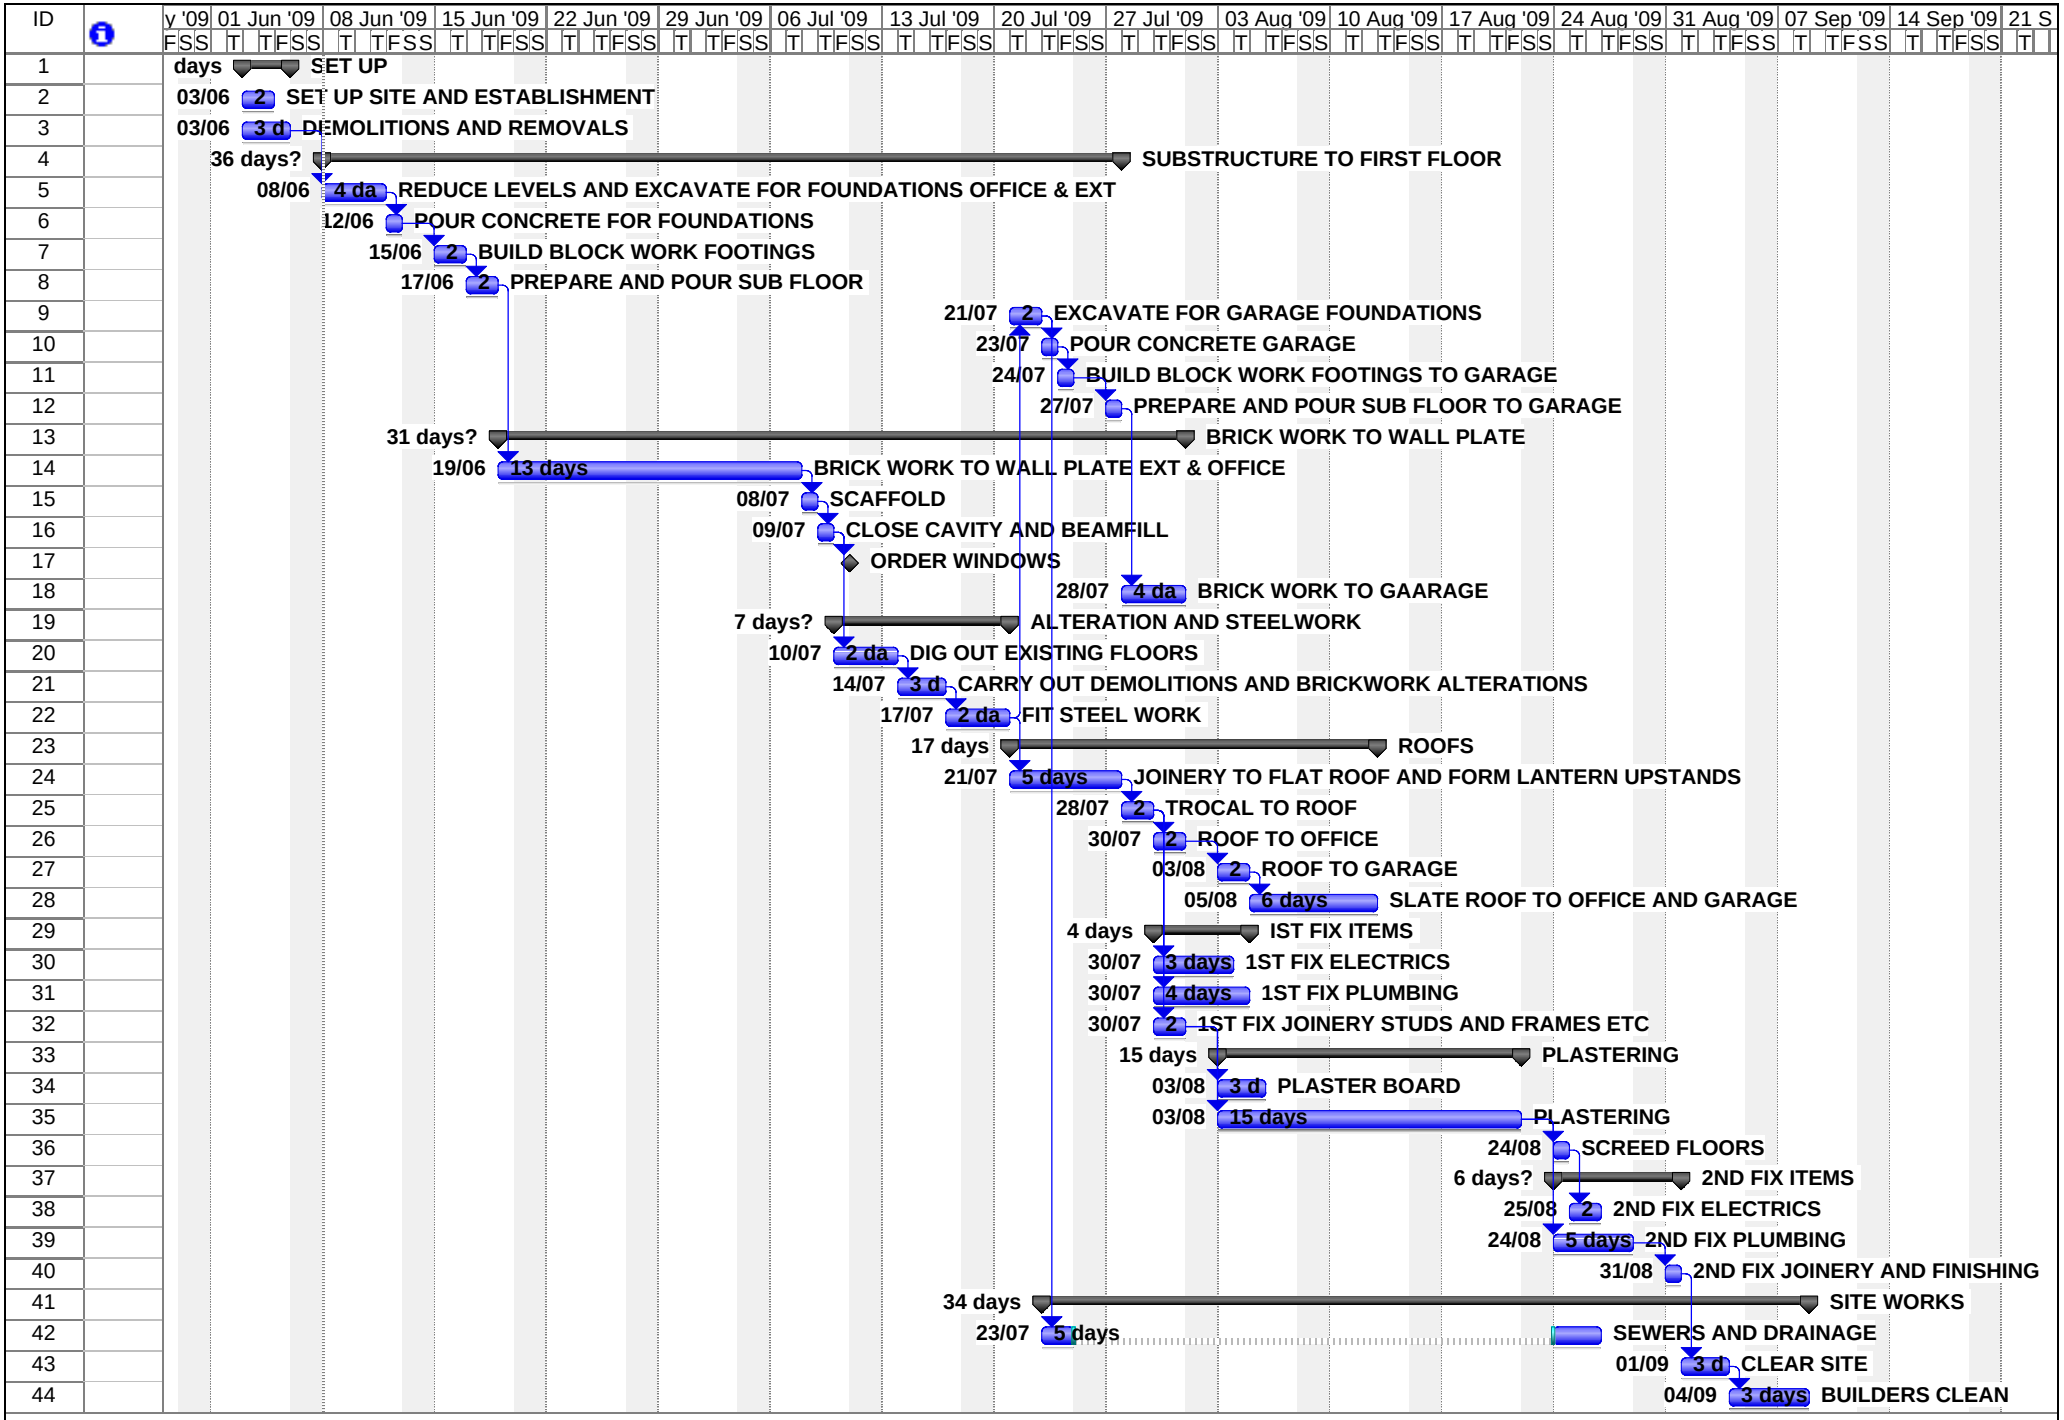
ID
y '09 01 Jun '09 08 Jun '09 15 Jun '09 22 Jun '09 29 Jun '09 06 Jul '09 13 Jul '09 20 Jul '09 27 Jul '09 03 Aug '09 10 Aug '09 17 Aug '09 24 Aug '09 31 Aug '09 07 Sep '09 14 Sep '09 21 S
1 days SET UP
2 03/06 2 SET UP SITE AND ESTABLISHMENT
3 03/06 3 d DEMOLITIONS AND REMOVALS
4 36 days? SUBSTRUCTURE TO FIRST FLOOR
5 08/06 4 da REDUCE LEVELS AND EXCAVATE FOR FOUNDATIONS OFFICE & EXT
6 12/06 POUR CONCRETE FOR FOUNDATIONS
7 15/06 2 BUILD BLOCK WORK FOOTINGS
8 17/06 2 PREPARE AND POUR SUB FLOOR
9 21/07 2 EXCAVATE FOR GARAGE FOUNDATIONS
10 23/07 POUR CONCRETE GARAGE
11 24/07 BUILD BLOCK WORK FOOTINGS TO GARAGE
12 27/07 PREPARE AND POUR SUB FLOOR TO GARAGE
13 31 days? BRICK WORK TO WALL PLATE
14 19/06 13 days BRICK WORK TO WALL PLATE EXT & OFFICE
15 08/07 SCAFFOLD
16 09/07 CLOSE CAVITY AND BEAMFILL
17 ORDER WINDOWS
18 28/07 4 da BRICK WORK TO GAARAGE
19 7 days? ALTERATION AND STEELWORK
20 10/07 2 da DIG OUT EXISTING FLOORS
21 14/07 3 d CARRY OUT DEMOLITIONS AND BRICKWORK ALTERATIONS
22 17/07 2 da FIT STEEL WORK
23 17 days ROOFS
24 21/07 5 days JOINERY TO FLAT ROOF AND FORM LANTERN UPSTANDS
25 28/07 2 TROCAL TO ROOF
26 30/07 2 ROOF TO OFFICE
27 03/08 2 ROOF TO GARAGE
28 05/08 6 days SLATE ROOF TO OFFICE AND GARAGE
29 4 days IST FIX ITEMS
30 30/07 3 days 1ST FIX ELECTRICS
31 30/07 4 days 1ST FIX PLUMBING
32 30/07 2 1ST FIX JOINERY STUDS AND FRAMES ETC
33 15 days PLASTERING
34 03/08 3 d PLASTER BOARD
35 03/08 15 days PLASTERING
36 24/08 SCREED FLOORS
37 6 days? 2ND FIX ITEMS
38 25/08 2 2ND FIX ELECTRICS
39 24/08 5 days 2ND FIX PLUMBING
40 31/08 2ND FIX JOINERY AND FINISHING
41 34 days SITE WORKS
42 23/07 5 days SEWERS AND DRAINAGE
43 01/09 3 d CLEAR SITE
44 04/09 3 days BUILDERS CLEAN
